




Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete	Calendar													
										Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q		
DCKA2019C0002-U13LA	<b>Reconstruction of Oregon Ave NW Look-Ahead !</b>	139	26-Jan-21	12-Nov-21	16-Dec-19		16-Dec-19	04-Dec-21															
<b>DCKA2019C0002-U13LA.1 PRE-CONSTRUCTION PHASE</b>																							
<b>DCKA2019C0002-U13LA.2 PROJECT MILESTONES</b>																							
MIL-1010	Finish Phase 1	0		26-Jan-21				05-Feb-21	0%														
MIL-1100	Finish Modified Phase 3D-1	0		06-Feb-21				17-Feb-21	0%														
MIL-1120	Start Modified Phase 3D-2	0	06-Feb-21					17-Feb-21	0%														
<b>DCKA2019C0002-U13LA.3 CONSTRUCTION PHASE</b>																							
<b>DCKA2019C0002-U13LA.3.7 Change Orders, Article 3 Directives and Additional Work</b>																							
<b>DCKA2019C0002-U13LA.3.7.1 Emergency Resurfacing b/w Military Rd &amp; Horse Stable Rd</b>																							
<b>DCKA2019C0002-U13LA.3.1 PHASE 1 (Oregon Ave b/w Beech St &amp; Western Ave NW)</b>																							
<b>DCKA2019C0002-U13LA.3.1.1 Phase 1A (Eastern Half b/w Beech St &amp; Western Ave NW)</b>																							
<b>DCKA2019C0002-U13LA.3.1.2 Phase 1A-1 (SE Corner- Oregon Ave, Chesnut St &amp; Wise Rd)</b>																							
<b>DCKA2019C0002-U13LA.3.1.3 Phase 1A-2 (NE Corner- Oregon Ave, Chesnut St &amp; Wise Rd)</b>																							
<b>DCKA2019C0002-U13LA.3.1.4 Phase 1B (Western Half b/w Beech St &amp; Western Ave NW)</b>																							
<b>DCKA2019C0002-U13LA.3.1.5 Phase 1B-1 (SW Corner- Oregon Ave, Chesnut St &amp; Wise Rd)</b>																							
<b>DCKA2019C0002-U13LA.3.1.6 Phase 1B-2 (NW Corner- Oregon Ave, Chesnut St &amp; Wise Rd)</b>																							
<b>DCKA2019C0002-U13LA.3.1.7 Phase 1C (Northern Half of Western Ave)</b>																							
<b>DCKA2019C0002-U13LA.3.2 PHASE 2 (Oregon Ave b/w Military Rd &amp; Rittenhouse St NW)</b>																							
<b>DCKA2019C0002-U13LA.3.2.1 Phase 2A (Eastern Half b/w Military Rd &amp; Rittenhouse St NW)</b>																							
P2A-1070	Install Watermain, Fire Hydrants, Gate Valves, Fittings & Appurtenances (Sta. 11+68 to 11+98)	6	26-Jan-21	26-Jan-21	23-Sep-20		03-Jun-21	03-Jun-21	98.99%														
P2A-1100	Install PCC Curb, Gutter, Top Soil & Seed (Rittenhouse St to Moreland Pl)	7	26-Jan-21	26-Jan-21	05-Oct-20		02-Jun-21	02-Jun-21	98.99%														
P2A-1120	Install Permeable Concrete Paver Type 2, Aggregates, Underdrains, Geotextile, Water	5	26-Jan-21	26-Jan-21	30-Oct-20		02-Jun-21	03-Jun-21	90%														
<b>DCKA2019C0002-U13LA.3.2.2 Phase 2A-1 (Eastern Half- Oregon Ave &amp; Horse Stable Rd)</b>																							
<b>DCKA2019C0002-U13LA.3.2.3 Phase 2B (Western Half b/w Military Rd &amp; Rittenhouse St NW)</b>																							
P2B-1090	Roadway Excavation, Install Bus Pads, Geotextile, Aggregate Base (Rittenhouse to M	9	26-Jan-21	26-Jan-21	16-Dec-20		03-Jun-21	03-Jun-21	98.01%														
P2B-1120	Install PCC Curb, Gutter, Wheelchair Ramps (Rittenhouse to Moreland Pl)	7	26-Jan-21	26-Jan-21	21-Dec-20		03-Jun-21	03-Jun-21	95%														
P2B-1140	Install Exposed Aggregate SW, & Property Driveway Entrances	7	26-Jan-21	30-Jan-21	21-Jan-21		12-Jun-21	16-Jun-21	60%														
P2B-1150	Install Bioretention Planters, Permeable Pavers, Infiltration Under SW, Underdrains (Ri	14	26-Jan-21	09-Feb-21	21-Jan-21		03-Jun-21	16-Jun-21	25%														
P2B-1160	Install Retaining Walls (1 & 2), Property Wall, and PCC Copings	5	26-Jan-21	29-Jan-21	12-Jan-21		14-Jun-21	16-Jun-21	60%														
P2B-1170	Install 8" HMA Base Course, 19mmn (2B)	7	09-Feb-21	12-Feb-21	07-Jan-21		16-Jun-21	19-Jun-21	60%														
<b>DCKA2019C0002-U13LA.3.2.4 Phase 2B-1 (Island Modification - Oregon Ave &amp; Clover Rd)</b>																							
<b>DCKA2019C0002-U13LA.3.3 PHASE 3 (Oregon Ave b/w Rittenhouse St &amp; Beech St NW)</b>																							
<b>DCKA2019C0002-U13LA.3.3.2 Modified Phase 3B (Eastern Half b/w Rittenhouse St &amp; Tennyson St)</b>																							
<b>DCKA2019C0002-U13LA.3.3.3 Modified Phase 3B-1 (Eastern Half - Oregon Ave &amp; Bingham Dr Inters)</b>																							
<b>DCKA2019C0002-U13LA.3.3.4 Modified Phase 3C (Western Half b/w Rittenhouse St &amp; Tennyson St)</b>																							
<b>DCKA2019C0002-U13LA.3.3.5 Modified Phase 3C-1 (Western Half - Oregon Ave &amp; Bingham Rd Inte)</b>																							
<b>DCKA2019C0002-U13LA.3.3.6 Modified Phase 3D-1 (Eastern Half of Oregon Ave b/w Tennyson St &amp; Moreland Pl)</b>																							
MP3D1-102	Install Catch Basins, Basin-Connect & Sewer Pipes, and Manholes	15	26-Jan-21	26-Jan-21	07-Jan-21		05-Feb-21	06-Feb-21	95%														
MP3D1-103	Roadway Excavation, Install Geotextile, Aggregate Base	7	26-Jan-21	04-Feb-21	26-Jan-21		06-Feb-21	13-Feb-21	10%														
MP3D1-104	Install PCC Curb, Gutter, and Wheelchair Ramps	5	30-Jan-21	05-Feb-21			13-Feb-21	20-Feb-21	0%														
MP3D1-105	Install 8" HMA Base Course, 19mmn (3D-1)	2	04-Feb-21	06-Feb-21			13-Feb-21	17-Feb-21	0%														
<b>DCKA2019C0002-U13LA.3.3.7 Modified Phase 3D-2 (Western Half of Oregon Ave b/w Tennyson St &amp; Moreland Pl)</b>																							
<b>DCKA2019C0002-U13LA.3.3.1 Phase 3A (Bridge Reconstruction of Pinehurst Branch)</b>																							
<b>DCKA2019C0002-U13LA.3.3.1.1 Bridge Work</b>																							
<b>DCKA2019C0002-U13LA.3.3.1.2 Utility Work &amp; Civil Work</b>																							
<b>DCKA2019C0002-U13LA.3.3.8 Phase 3E (Entire Roadway Section b/w Oregon Knolls Dr &amp; Private I</b>																							

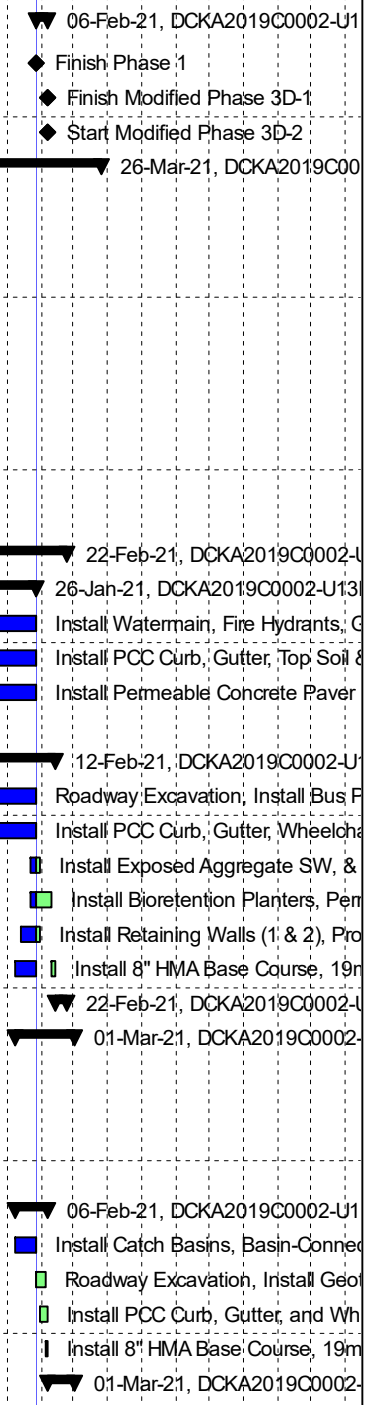

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD01-26-21)

DCKA2019C0002-U13LA

3-Week Look-Ahead © Oracle Corporation



Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete	Gantt Chart											
										Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q
<b>DCKA2019C0002-U13LA.3.4 Traffic &amp; Streetlight Work</b>																					
TR-1000	Remove Existing Streetlights & Install New Poles, Arm, Luminaires (Phase 1) Western	7	26-Jan-21	03-Feb-21			15-Sep-21	23-Sep-21	0%												
TR-1010	Remove Existing Streetlights & Install New Poles, Arm, Luminaires (Phase 1) Dogwood	7	04-Feb-21	11-Feb-21			23-Sep-21	04-Oct-21	0%												
TR-1050	Install Traffic Foundation, Cabinet, Controller, Pole, Lights (Oregon Ave & Military Rd)	14	13-Mar-21	26-Mar-21	04-Nov-20		21-Oct-21	05-Nov-21	20%												
<b>DCKA2019C0002-U13LA.3.5 Paving, Line Stiping, Signage, and Miscellaneous Work</b>																					
<b>DCKA2019C0002-U13LA.3.6 Landscape Work</b>																					
<b>DCKA2019C0002-U13LA.4 LUMPSUM ITEMS (Non-Construction)</b>																					
<b>DCKA2019C0002-U13LA.5 POST-CONSTRUCTION PHASE</b>																					
<b>DCKA2019C0002-U13LA.6 Delays, Additional Work, and Changes</b>																					

- Remaining Level ...
- Actual Level of Ef...
- Actual Work
- Remaining Work
- Critical Remaining...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD01-26-21)

DCKA2019C0002-U13LA

3-Week Look-Ahead® Oracle Corporation

