

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete	Remarks	Q	Q	Q	Q	Q	Q	Q	Q	Q
											J	J	J	J	J	J	J	J	J
Oregon-LA-05-31-21 Reconstruction of Oregon Ave NW Look-Ahead Sched		180	01-Jun-21	16-Oct-21	04-Nov-20		08-Apr-21	05-Nov-21											
Oregon-LA-05-31-21.1 PRE-CONSTRUCTION PHASE		0																	
Oregon-LA-05-31-21.2 PROJECT MILESTONES		9	01-Jun-21	11-Jun-21			19-Apr-21	17-Sep-21											
MIL-1030	Finish Phase 2	0		10-Jun-21				19-Apr-21	0%										
MIL-1050	Finish Modified Phase 3B & 3B-1	0		10-Jun-21				01-Sep-21	0%										
MIL-1060	Start Modified Phase 3C & 3C-1	0	11-Jun-21				01-Sep-21		0%										
MIL-1130	Finish Modified Phase 3C-2	0		01-Jun-21				17-Sep-21	0%										
MIL-1140	Start Phase 3A	0	11-Jun-21				19-Apr-21		0%										
Oregon-LA-05-31-21.3 CONSTRUCTION PHASE		180	01-Jun-21	16-Oct-21	04-Nov-20		08-Apr-21	05-Nov-21											
Oregon-LA-05-31-21.3.7 Change Orders, Article 3 Directives and Additional Work		0																	
Oregon-LA-05-31-21.3.7.1 Emergency Resurfacing b/w Military Rd & Horse Stable Rd		0																	
Oregon-LA-05-31-21.3.1 PHASE 1 (Oregon Ave b/w Beech St & Western Ave NW)		0																	
Oregon-LA-05-31-21.3.1.1 Phase 1A (Eastern Half b/w Beech St & Western Ave NW)		0																	
Oregon-LA-05-31-21.3.1.2 Phase 1A-1 (SE Corner- Oregon Ave, Chesnut St & Wise Rd)		0																	
Oregon-LA-05-31-21.3.1.3 Phase 1A-2 (NE Corner- Oregon Ave, Chesnut St & Wise Rd)		0																	
Oregon-LA-05-31-21.3.1.4 Phase 1B (Western Half b/w Beech St & Western Ave NW)		0																	
Oregon-LA-05-31-21.3.1.5 Phase 1B-1 (SW Corner- Oregon Ave, Chesnut St & Wise Rd)		0																	
Oregon-LA-05-31-21.3.1.6 Phase 1B-2 (NW Corner- Oregon Ave, Chesnut St & Wise Rd)		0																	
Oregon-LA-05-31-21.3.1.7 Phase 1C (Nortnen Half of Western Ave)		0																	
Oregon-LA-05-31-21.3.2 PHASE 2 (Oregon Ave b/w Military Rd & Rittenhouse St NW)		8	01-Jun-21	10-Jun-21			08-Apr-21	19-Apr-21											
Oregon-LA-05-31-21.3.2.1 Phase 2A (Eastern Half b/w Military Rd & Rittenhouse St NW)		0																	
Oregon-LA-05-31-21.3.2.2 Phase 2A-1 (Eastern Half- Oregon Ave & Horse Stable Rd)		0																	
Oregon-LA-05-31-21.3.2.3 Phase 2B (Western Half b/w Military Rd & Rittenhouse St NW)		0																	
Oregon-LA-05-31-21.3.2.4 Phase 2B-1 (Island Modification - Oregon Ave & Clover Rd)		9	01-Jun-21	10-Jun-21			08-Apr-21	19-Apr-21											
P2B1-1000	Demolish East Side Curb of Existing Island (Military Rd, Oregon Ave & Clover Rd)	7	01-Jun-21	08-Jun-21			08-Apr-21	16-Apr-21	0%	Waiting for NPS Approval									
P2B1-1010	Install PCC Curb, Gutter; Restore Roadway, Install Directional Island	2	09-Jun-21	10-Jun-21			16-Apr-21	19-Apr-21	0%	Waiting for NPS Approval									
Oregon-LA-05-31-21.3.3 PHASE 3 (Oregon Ave b/w Rittenhouse St & Beech St NW)		159	01-Jun-21	16-Oct-21	10-Mar-21		19-Apr-21	27-Oct-21											
Oregon-LA-05-31-21.3.3.2 Modified Phase 3B (Eastern Half b/w Rittenhouse St & Tennyson St NW)		0																	
Oregon-LA-05-31-21.3.3.3 Modified Phase 3B-1 (Eastern Half - Oregon Ave & Bingham Dr Intersection)		0																	
Oregon-LA-05-31-21.3.3.4 Modified Phase 3C (Western Half b/w Rittenhouse St & Tennyson St NW)		16	11-Jun-21	01-Jul-21			01-Sep-21	21-Sep-21											
MP3C-1000	Install Maintenance of Traffic/Erosion & Sediment Control Devices; Test Pit, Remove T	1	11-Jun-21	11-Jun-21			01-Sep-21	02-Sep-21	0%										
MP3C-1010	Install Electric Manholes, Conduits, and Concrete Enclosures (Nebraska Ave; Rittenho	6	12-Jun-21	19-Jun-21			02-Sep-21	10-Sep-21	0%										
MP3C-1020	Install Catch Basins, Basin-Connect & Sewer Pipes, and Manholes (Rittenhouse St to	12	16-Jun-21	01-Jul-21			07-Sep-21	21-Sep-21	0%										
Oregon-LA-05-31-21.3.3.5 Modified Phase 3C-1 (Western Half - Oregon Ave & Bingham Rd Intersection)		6	11-Jun-21	17-Jun-21			19-Oct-21	27-Oct-21											
MP3C1-1000	Install Watermain, Gate Valves, Fittings & Appurtenances	1	11-Jun-21	11-Jun-21			19-Oct-21	20-Oct-21	0%										
MP3C1-1010	Roadway Excavation, Install Geotextile, Aggregate Base (3C-1)	1	14-Jun-21	14-Jun-21			21-Oct-21	23-Oct-21	0%										
MP3C1-1020	Install PCC Curb, Gutter, Wheel Chair Ramps, Exposed Sidewalk	1	16-Jun-21	16-Jun-21			25-Oct-21	26-Oct-21	0%										
MP3C1-1030	Install 8" HMA Base Course, 19mmn (3C-1)	1	17-Jun-21	17-Jun-21			26-Oct-21	27-Oct-21	0%										
Oregon-LA-05-31-21.3.3.6 Modified Phase 3B-2 (Eastern Half of Oregon Ave b/w Tennyson St & Oreg		0																	
Oregon-LA-05-31-21.3.3.7 Modified Phase 3C-2 (Western Half of Oregon Ave b/w Tennyson St & Oreg		10	01-Jun-21	01-Jun-21	10-Mar-21		17-Sep-21	17-Sep-21											
MP3D2-1050	Install Electric Manholes, Conduits, and Concrete Enclosures (Tennyson St to Unicor	5	01-Jun-21	01-Jun-21	10-Mar-21		17-Sep-21	17-Sep-21	95%	1 6x18 CIP MH remaining on Unicor									
MP3D2-1060	Install Electric Manholes, Conduits, and Concrete Enclosures (Unicom Lane to Oreg	5	01-Jun-21	01-Jun-21	10-Mar-21		17-Sep-21	17-Sep-21	95%	1 6x18 CIP MH remaining on Unicor									
Oregon-LA-05-31-21.3.3.1 Phase 3A (Bridge Reconstruction of Pinehurst Branch)		122	11-Jun-21	16-Oct-21	10-May-21		19-Apr-21	08-Sep-21											
Oregon-LA-05-31-21.3.3.1.1 Bridge Work		7	12-Jun-21	21-Jun-21			20-Apr-21	29-Apr-21											
P3A-B-1020	North & South Abutment Install Stream Diversion	3	12-Jun-21	15-Jun-21			20-Apr-21	24-Apr-21	0%										
P3A-B-1030	North & South Abutment Excavation	4	16-Jun-21	21-Jun-21			24-Apr-21	29-Apr-21	0%										


- Remaining Level ...
- Actual Level of Ef...
- Actual Work
- Remaining Work
- Critical Remaining...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD 05-31-21)

Oregon-LA-05-31-21

3-Week Look-Ahead © Oracle Corporation

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete	Remarks	Q	Q	Q	Q	Q	Q	Q	Q	Q
Oregon-LA-05-31-21.3.3.1.2 Utility Work & Civil Work		122	11-Jun-21	16-Oct-21	10-May-21		19-Apr-21	08-Sep-21											
P3A-SW-10	Install Watermain, Gate Valves, Fittings & Appurtenances (Sta. 45+03 to 41+40)	14	15-Oct-21	16-Oct-21	13-May-21		07-Sep-21	08-Sep-21	90%	On-going -PCC Encased 12" waterma									
P3A-SW-10:	Install Sewer Manhole, 21" Sanitary Sewer, and Outfalls 5 & 6 (3A)	10	11-Jun-21	11-Jun-21	10-May-21		19-Apr-21	20-Apr-21	90%	Started yesterday, will continue for the									
Oregon-LA-05-31-21.3.3.8 Phase 3E (Entire Roadway Section b/w Oregon Knolls Dr & Private Drivewa		0																	
Oregon-LA-05-31-21.3.4 Traffic & Streetlight Work		14	11-Jun-21	25-Jun-21	04-Nov-20		21-Oct-21	05-Nov-21											
TR-1050	Install Traffic Foundation, Cabinet, Controller, Pole, Lights (Oregon Ave & Military Rd)	14	11-Jun-21	25-Jun-21	04-Nov-20		21-Oct-21	05-Nov-21	20%	Waiting for RFI No. 5-1, Feed Point									
Oregon-LA-05-31-21.3.5 Paving, Line Stiping, Signage, and Miscellaneous Work		66	01-Jun-21	01-Jun-21	28-Dec-20		23-Oct-21	30-Oct-21											
PV-1010	Install 2" HMA Surface Course, 12.5mm (Phase 2) Mill & Pave Sub-Phases Limits	5	01-Jun-21	01-Jun-21	23-Apr-21		23-Oct-21	23-Oct-21	98%	98% Complete. Only remaining is the									
PV-1040	Line Striping and Pavement Marking (Phase 2)	5	01-Jun-21	01-Jun-21	24-Apr-21		30-Oct-21	30-Oct-21	98%	98% Complete. Only remaining is the									
PV-1064	Install Permanent Traffic Signs (Phase 2)	5	01-Jun-21	01-Jun-21	28-Dec-20		30-Oct-21	30-Oct-21	98%	98% Complete. Only remaining is the									
Oregon-LA-05-31-21.3.6 Landscape Work		0																	
Oregon-LA-05-31-21.4 LUMPSUM ITEMS (Non-Construction)		0																	
Oregon-LA-05-31-21.5 POST-CONSTRUCTION PHASE		0																	
Oregon-LA-05-31-21.6 Delays, Additional Work, and Changes		5	01-Jun-21	05-Jun-21			30-Oct-21	05-Nov-21											

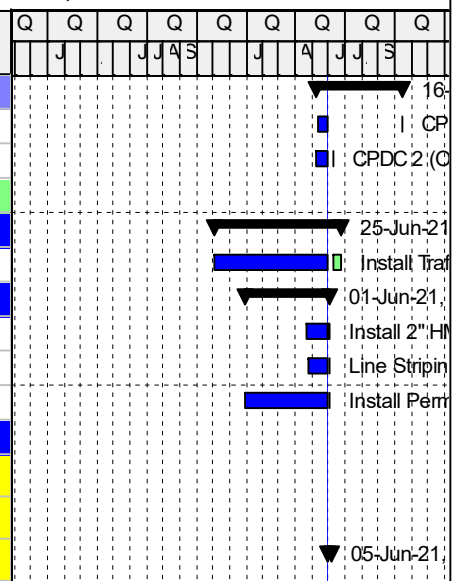

- Remaining Level ...
- Actual Level of Ef...
- Actual Work
- Remaining Work
- Critical Remaining...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD 05-31-21)

Oregon-LA-05-31-21

3-Week Look-Ahead © Oracle Corporation
