


Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Activity % Complete	Calendar																								
								Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q	Q													
								N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N
MP3D2-109	Install PCC Curb, Gutter, and Wheelchair Ramps	5	01-Apr-21	06-Apr-21			0%																									
MP3D2-110	Installation of Driveways and Exposed Aggregate Sidewalk	5	07-Apr-21	12-Apr-21			0%																									
DCKA2019C0002-LA3-22.3.3.1 Phase 3A (Bridge Reconstruction of Pinehurst Branch)		0																														
DCKA2019C0002-LA3-22.3.3.1.1 Bridge Work		0																														
DCKA2019C0002-LA3-22.3.3.1.2 Utility Work & Civil Work		0																														
DCKA2019C0002-LA3-22.3.3.8 Phase 3E (Entire Roadway Section b/w Oregon Knolls Dr & Private Driveway)		0																														
DCKA2019C0002-LA3-22.3.4 Traffic & Streetlight Work		14	03-Apr-21	17-Apr-21	04-Nov-20																											
TR-1020	Remove Existing Streetlights & Install New Poles, Arm, Luminaires (Phase 2) Rittenhouse St to Moreland Pl	7	03-Apr-21	05-Apr-21	01-Mar-21		95%																									
TR-1050	Install Traffic Foundation, Cabinet, Controller, Pole, Lights (Oregon Ave & Military Rd)	14	05-Apr-21	17-Apr-21	04-Nov-20		20%																									
DCKA2019C0002-LA3-22.3.5 Paving, Line Stiping, Signage, and Miscellaneous Work		45	23-Mar-21	05-Apr-21	28-Dec-20																											
DCKA2019C0002-LA3-22.3.6 Landscape Work		7	22-Mar-21	29-Mar-21																												
DCKA2019C0002-LA3-22.4 LUMPSUM ITEMS (Non-Construction)		0																														
DCKA2019C0002-LA3-22.5 POST-CONSTRUCTION PHASE		0																														
DCKA2019C0002-LA3-22.6 Delays, Additional Work, and Changes		5	22-Mar-21	26-Mar-21																												

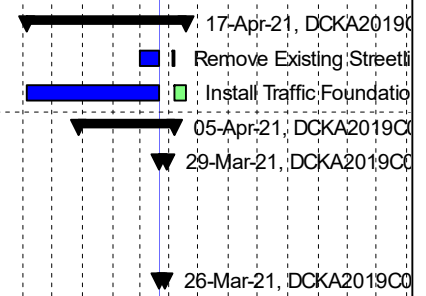

- Remaining Level ...
- Actual Level of Ef...
- Actual Work
- Remaining Work
- Critical Remaining...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD03-22-21)

DCKA2019C0002-LA3-22

3-Week Look-Ahead © Oracle Corporation

