Data Date: 03-May-21

Capitol Paving of D.C., Inc.

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete
Oregon-LA-05-03-21	Reconstruction of Oregon Ave NW Look-Ahead Schedu	84	03-May-21	01-Jun-21	04-Nov-20		23-Mar-21	22-Nov-21	
Oregon-LA-05-03-21.1	PRE-CONSTRUCTION PHASE	0							
Oregon-LA-05-03-21.2	PROJECT MILESTONES	3	08-May-21	13-May-21			03-Apr-21	17-Sep-21	
MIL-1030	Finish Phase 2	0		12-May-21				03-Apr-21	0%
MIL-1130	Finish Modified Phase 3C-2	0		08-May-21				17-Sep-21	0%
MIL-1140	Start Phase 3A	0	13-May-21				03-Apr-21		0%
Oregon-LA-05-03-21.3	CONSTRUCTION PHASE	84	03-May-21	01-Jun-21	04-Nov-20		23-Mar-21	22-Nov-21	
Oregon-LA-05-03-21.3.7	Change Orders, Article 3 Directives and Additional Work	0							
Oregon-LA-05-03-21.3.7.1	Emergency Resurfacing b/w Military Rd & Horse Stable Rd	0							
Oregon-LA-05-03-21.3.1	PHASE 1 (Oregon Ave b/w Beech St & Western Ave NW)	0							
Oregon-LA-05-03-21.3.1.1	Phase 1A (Eastern Half b/w Beech St & Western Ave NW)	0							
Oregon-LA-05-03-21.3.1.2	Phase 1A-1 (SE Corner- Oregon Ave, Chesnut St & Wise Rd)	0							
Oregon-LA-05-03-21.3.1.3	Phase 1A-2 (NE Corner- Oregon Ave, Chesnut St & Wise Rd)	0							
Oregon-LA-05-03-21.3.1.4	Phase 1B (Western Half b/w Beech St & Western Ave NW)	0							
Oregon-LA-05-03-21.3.1.5	Phase 1B-1 (SW Corner- Oregon Ave, Chesnut St & Wise Rd)	0							
Oregon-LA-05-03-21.3.1.6	Phase 1B-2 (NW Corner- Oregon Ave, Chesnut St & Wise Rd)	0							
Oregon-LA-05-03-21.3.1.7	Phase 1C (Northen Half of Western Ave)	0							
Oregon-LA-05-03-21.3.2	PHASE 2 (Oregon Ave b/w Military Rd & Rittenhouse St NW)	8	03-May-21	12-May-21			23-Mar-21	03-Apr-21	
Oregon-LA-05-03-21.3.2.1	Phase 2A (Eastern Half b/w Military Rd & Rittenhouse St NW)	0							
Oregon-LA-05-03-21.3.2.2	Phase 2A-1 (Eastern Half- Oregon Ave & Horse Stable Rd)	0							
Oregon-LA-05-03-21.3.2.3	Phase 2B (Western Half b/w Military Rd & Rittenhouse St NW)	0							
Oregon-LA-05-03-21.3.2.4	Phase 2B-1 (Island Modification - Oregon Ave & Clover Rd)	9	03-May-21	12-May-21			23-Mar-21	03-Apr-21	
P2B1-1000	Demolish East Side Curb of Existing Island (Military Rd, Oregon Ave & Clover Rd)	7	03-May-21	10-May-21			23-Mar-21	01-Apr-21	0%
P2B1-1010	Install PCC Curb, Gutter; Restore Roadway, Install Directional Island	2	11-May-21	12-May-21			01-Apr-21	03-Apr-21	0%
Oregon-LA-05-03-21.3.3	PHASE 3 (Oregon Ave b/w Rittenhouse St & Beech St NW)	63	03-May-21	01-Jun-21	10-Mar-21		03-Apr-21	17-Sep-21	
Oregon-LA-05-03-21.3.3.2	Modified Phase 3B (Eastern Half b/w Rittenhouse St & Tennyson St NW)	46	13-May-21	01-Jun-21	02-Apr-21		11-Aug-21	26-Aug-21	
MP3B-1010	Install Electric Manholes, Conduits, and Concrete Enclosures (3B)	14	13-May-21	14-May-21	02-Apr-21		11-Aug-21	12-Aug-21	90%
MP3B-1020	Install Catch Basins, Basin-Connect & Sewer Pipes, MH, & Outfall #4 (Rittenhouse St	14	14-May-21	18-May-21	29-Apr-21		12-Aug-21	16-Aug-21	80%
MP3B-1030	Roadway Excavation, Install Geotextile, Aggregate Base (3B)	15	18-May-21	28-May-21	02-Apr-21		16-Aug-21	24-Aug-21	50%
MP3B-1040	Install Bioswale, PCC Curb, Gutter & Top Soil & Seed (3B), and LID 7-3	12	18-May-21	01-Jun-21	04-May-21		16-Aug-21	26-Aug-21	20%
Oregon-LA-05-03-21.3.3.3	Modfied Phase 3B-1 (Eastern Half - Oregon Ave & Bingham Dr Intersection)	24	13-May-21	20-May-21	07-Apr-21		26-Aug-21	04-Sep-21	
MP3B1-1000	Install Electric Conduits, and Concrete Enclosures	1	13-May-21	13-May-21	07-Apr-21		26-Aug-21	26-Aug-21	90%
MP3B1-1010	Install Catch Basins, Basin-Connect & Sewer Pipes, Manhole	1	13-May-21	13-May-21	29-Apr-21		26-Aug-21	26-Aug-21	80%
MP3B1-1020	Roadway Excavation, Install Geotextile, Aggregate Base (3B-1)	7	13-May-21	20-May-21	08-Apr-21		26-Aug-21	04-Sep-21	15%
MP3B1-1030	Demolish Existing Pavement & Install New Curb & Gutter	2	13-May-21	15-May-21			26-Aug-21	30-Aug-21	0%
MP3B1-1040	Install 8" HMA Base Course, 19mmn (3B-1)	1	15-May-21	17-May-21			30-Aug-21	01-Sep-21	0%
Oregon-LA-05-03-21.3.3.4	Modified Phase 3C (Western Half b/w Rittenhouse St & Tennyson St NW)	0							
Oregon-LA-05-03-21.3.3.5	Modified Phase 3C-1 (Western Half - Oregon Ave & Bingham Rd Intersectio	0							
Oregon-LA-05-03-21.3.3.6	Modified Phase 3B-2 (Eastern Half of Oregon Ave b/w Tennyson St & Orego	0							
Oregon-LA-05-03-21.3.3.7	Modified Phase 3C-2 (Western Half of Oregon Ave b/w Tennyson St & Oregc	52	03-May-21	08-May-21	10-Mar-21		11-Sep-21	17-Sep-21	
MP3D2-1050	Install Electric Manholes, Conduits, and Concrete Enclosures (Tennyson St to Unicorr	5	03-May-21	03-May-21	10-Mar-21		11-Sep-21	11-Sep-21	90%
MP3D2-1060	Install Electric Manholes, Conduits, and Concrete Enclosures (Unicorn Lane to Oregor	5	03-May-21	03-May-21	10-Mar-21		11-Sep-21	13-Sep-21	90%
MP3D2-1110	Install Porous Flexible, Bioretention Facilities, Topsoil and Seed	15	04-May-21	08-May-21	23-Apr-21		13-Sep-21	17-Sep-21	70%
MP3D2-1120	Install 8" HMA Base Course, 19mmn (3D-2)	4	08-May-21	08-May-21	15-Apr-21		17-Sep-21	17-Sep-21	95%
Oregon-LA-05-03-21.3.3.1	Phase 3A (Bridge Reconstruction of Pinehurst Branch)	17	13-May-21	26-May-21	28-Apr-21		03-Apr-21	15-Apr-21	
Oregon-LA-05-03-21.3.3.1.1	Bridge Work	0							

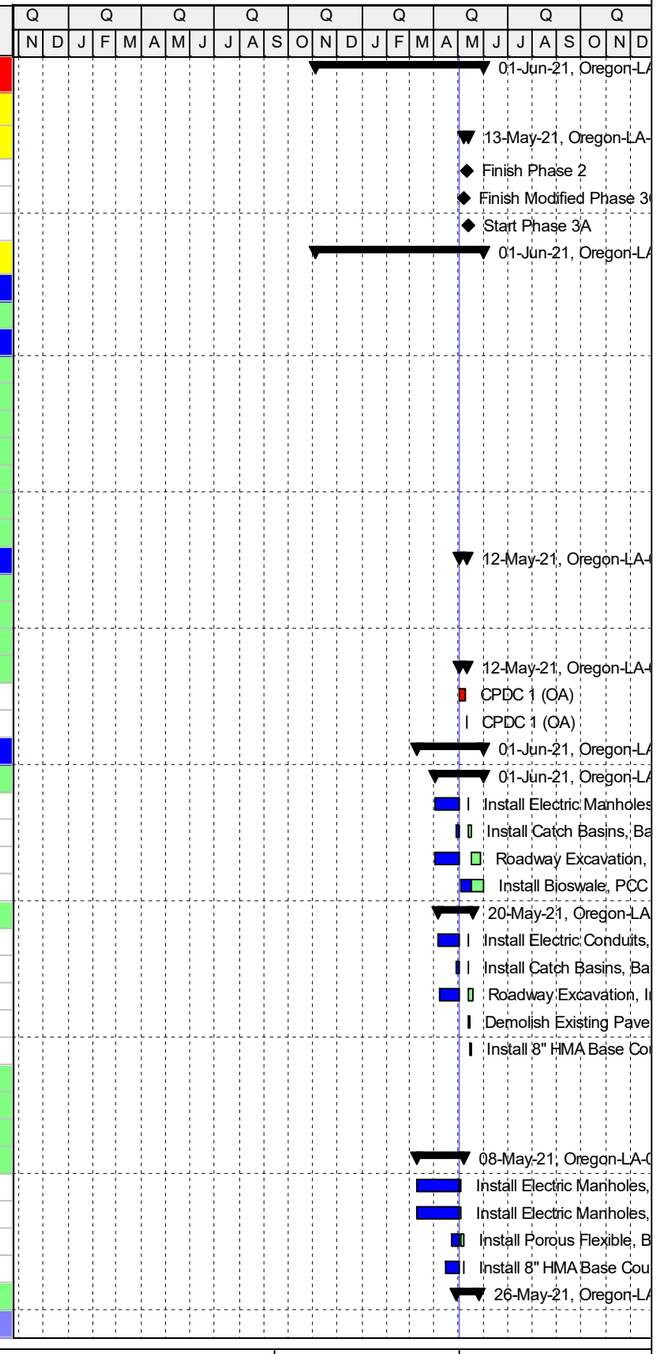

Remaining Level ...
Actual Level of Ef...
Actual Work
Remaining Work
Critical Remaining...

3-Week Look-Ahead

© Oracle Corporation

Data Date: 03-May-21

Capitol Paving of D.C., Inc.

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete
Oregon-LA-05-03-21.3.3.1.2	**Utility Work & Civil Work**	20	13-May-21	26-May-21	28-Apr-21		03-Apr-21	15-Apr-21	
P3A-SW-10(	Remove Existing Trees	1	13-May-21	13-May-21	28-Apr-21		03-Apr-21	03-Apr-21	75%
P3A-SW-10:	Install Sewer Manhole, 21" Sanitary Sewer, and Outfalls 5 & 6 (3A)	10	13-May-21	26-May-21			03-Apr-21	15-Apr-21	0%
Oregon-LA-05-03-21.3.3.8	**Phase 3E (Entire Roadway Section b/w Oregon Knolls Dr & Private Drivewa**	0							
Oregon-LA-05-03-21.3.4	**Traffic & Streetlight Work**	14	13-May-21	28-May-21	04-Nov-20		21-Oct-21	05-Nov-21	
TR-1050	Install Traffic Foundation, Cabinet, Controller, Pole, Lights (Oregon Ave & Military Rd)	14	13-May-21	28-May-21	04-Nov-20		21-Oct-21	05-Nov-21	20%
Oregon-LA-05-03-21.3.5	**Paving, Line Stiping, Signage, and Miscellaneous Work**	66	03-May-21	03-May-21	28-Dec-20		23-Oct-21	30-Oct-21	
PV-1010	Install 2" HMA Surface Course, 12.5mm (Phase 2) Mill & Pave Sub-Phases Limits	5	03-May-21	03-May-21	23-Apr-21		23-Oct-21	23-Oct-21	98%
PV-1040	Line Striping and Pavement Marking (Phase 2)	5	03-May-21	03-May-21	24-Apr-21		30-Oct-21	30-Oct-21	98%
PV-1064	Install Permanent Traffic Signs (Phase 2)	5	03-May-21	03-May-21	28-Dec-20		30-Oct-21	30-Oct-21	98%
Oregon-LA-05-03-21.3.6	**Landscape Work**	5	03-May-21	07-May-21			16-Nov-21	22-Nov-21	
LS-0080	Install Bioretention Railing Fence (Phase 2)	5	03-May-21	07-May-21			16-Nov-21	22-Nov-21	0%
Oregon-LA-05-03-21.4	**LUMPSUM ITEMS (Non-Construction)**	0							
Oregon-LA-05-03-21.5	**POST-CONSTRUCTION PHASE**	0							
Oregon-LA-05-03-21.6	**Delays, Additional Work, and Changes**	5	03-May-21	07-May-21			30-Oct-21	05-Nov-21	

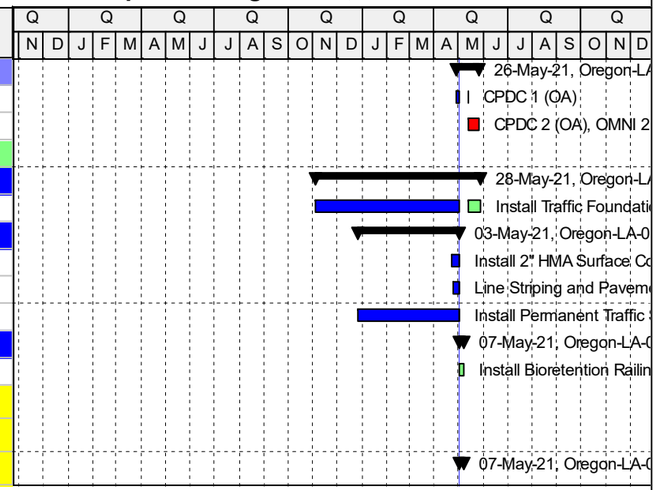

© Oracle Corporation
