Data Date: 22-Feb-21

Capitol Paving of D.C., Inc.

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete
DCKA2019C0002-LA14	**Reconstruction of Oregon Ave NW Look-Ahead Sc**	143	22-Feb-21	19-Nov-21	16-Dec-19		16-Dec-19	04-Dec-21	
DCKA2019C0002-LA14.1	**PRE-CONSTRUCTION PHASE**	0							
DCKA2019C0002-LA14.2	**PROJECT MILESTONES**	13	22-Feb-21	10-Mar-21			13-Feb-21	01-Jul-21	
MIL-1010	Finish Phase 1	0		22-Feb-21				13-Feb-21	0%
MIL-1030	Finish Phase 2	0		10-Mar-21				01-Jul-21	0%
MIL-1040	Start Modified Phase 3B & 3B-1	0	10-Mar-21				01-Jul-21		0%
MIL-1100	Finish Modified Phase 3B-2	0		24-Feb-21				17-Feb-21	0%
MIL-1120	Start Modified Phase 3C-2	0	24-Feb-21				17-Feb-21		0%
DCKA2019C0002-LA14.3	**CONSTRUCTION PHASE**	143	22-Feb-21	10-Apr-21	23-Sep-20		13-Feb-21	22-Nov-21	
DCKA2019C0002-LA14.3.7	**Change Orders, Article 3 Directives and Additional Work**	0							
DCKA2019C0002-LA14.3.7.1	**Emergency Resurfacing b/w Military Rd & Horse Stable Rd**	0							
DCKA2019C0002-LA14.3.1	**PHASE 1 (Oregon Ave b/w Beech St & Western Ave NW)**	0							
DCKA2019C0002-LA14.3.1.1	**Phase 1A (Eastern Half b/w Beech St & Western Ave NW)**	0							
DCKA2019C0002-LA14.3.1.2	**Phase 1A-1 (SE Corner- Oregon Ave, Chesnut St & Wise Rd)**	0							
DCKA2019C0002-LA14.3.1.3	**Phase 1A-2 (NE Corner- Oregon Ave, Chesnut St & Wise Rd)**	0							
DCKA2019C0002-LA14.3.1.4	**Phase 1B (Western Half b/w Beech St & Western Ave NW)**	0							
DCKA2019C0002-LA14.3.1.5	**Phase 1B-1 (SW Corner- Oregon Ave, Chesnut St & Wise Rd)**	0							
DCKA2019C0002-LA14.3.1.6	**Phase 1B-2 (NW Corner- Oregon Ave, Chesnut St & Wise Rd)**	0							
DCKA2019C0002-LA14.3.1.7	**Phase 1C (Northen Half of Western Ave)**	0							
DCKA2019C0002-LA14.3.2	**PHASE 2 (Oregon Ave b/w Military Rd & Rittenhouse St NW)**	129	22-Feb-21	10-Mar-21	23-Sep-20		14-Jun-21	01-Jul-21	
DCKA2019C0002-LA14.3.2.1	**Phase 2A (Eastern Half b/w Military Rd & Rittenhouse St NW)**	44	22-Feb-21	22-Feb-21	23-Sep-20		14-Jun-21	14-Jun-21	
P2A-1070	Install Watermain, Fire Hydrants, Gate Valves, Fittings & Appurtenances (Sta. 11+68 to 7+7	6	22-Feb-21	22-Feb-21	23-Sep-20		14-Jun-21	14-Jun-21	98.99%
P2A-1100	Install PCC Curb, Gutter, Top Soil & Seed (Rittenhouse St to Moreland Pl)	7	22-Feb-21	22-Feb-21	05-Oct-20		14-Jun-21	14-Jun-21	98.99%
P2A-1120	Install Permeable Concrete Paver Type 2, Aggregates, Underdrains, Geotextile, Waterproo	5	22-Feb-21	22-Feb-21	30-Oct-20		14-Jun-21	14-Jun-21	98%
DCKA2019C0002-LA14.3.2.2	**Phase 2A-1 (Eastern Half- Oregon Ave & Horse Stable Rd)**	0							
DCKA2019C0002-LA14.3.2.3	**Phase 2B (Western Half b/w Military Rd & Rittenhouse St NW)**	32	22-Feb-21	27-Feb-21	25-Nov-20		14-Jun-21	19-Jun-21	
P2B-1150	Install Bioretention Planters, Permeable Pavers, Infiltration Under SW, Underdrains (Rittenh	14	22-Feb-21	24-Feb-21	19-Jan-21		14-Jun-21	17-Jun-21	80%
P2B-1155	Install Bioretention Planters, Permeable Pavers, Infiltration Under SW, Underdrains (Morela	14	22-Feb-21	23-Feb-21	25-Nov-20		16-Jun-21	17-Jun-21	90%
P2B-1170	Install 8" HMA Base Course, 19mmn (2B)	7	24-Feb-21	27-Feb-21	07-Jan-21		17-Jun-21	19-Jun-21	80%
DCKA2019C0002-LA14.3.2.4	**Phase 2B-1 (Island Modification - Oregon Ave & Clover Rd)**	9	27-Feb-21	10-Mar-21			19-Jun-21	01-Jul-21	
DCKA2019C0002-LA14.3.3	**PHASE 3 (Oregon Ave b/w Rittenhouse St & Beech St NW)**	42	22-Feb-21	30-Mar-21	26-Jan-21		13-Feb-21	24-Aug-21	
DCKA2019C0002-LA14.3.3.2	**Modified Phase 3B (Eastern Half b/w Rittenhouse St & Tennyson St NW)**	17	10-Mar-21	30-Mar-21			01-Jul-21	23-Jul-21	
DCKA2019C0002-LA14.3.3.3	**Modfied Phase 3B-1 (Eastern Half - Oregon Ave & Bingham Dr Intersectio**	4	10-Mar-21	15-Mar-21			19-Aug-21	24-Aug-21	
DCKA2019C0002-LA14.3.3.4	**Modified Phase 3C (Western Half b/w Rittenhouse St & Tennyson St NW)**	0							
DCKA2019C0002-LA14.3.3.5	**Modified Phase 3C-1 (Western Half - Oregon Ave & Bingham Rd Intersecti**	0							
DCKA2019C0002-LA14.3.3.6	**Modified Phase 3B-2 (Eastern Half of Oregon Ave b/w Tennyson St & Oreg**	21	22-Feb-21	24-Feb-21	26-Jan-21		13-Feb-21	17-Feb-21	
MP3D1-103	Roadway Excavation, Install Geotextile, Aggregate Base	7	22-Feb-21	22-Feb-21	26-Jan-21		13-Feb-21	13-Feb-21	95%
MP3D1-105	Install 8" HMA Base Course, 19mmn (3D-1)	2	22-Feb-21	24-Feb-21			13-Feb-21	17-Feb-21	0%
DCKA2019C0002-LA14.3.3.7	**Modified Phase 3C-2 (Western Half of Oregon Ave b/w Tennyson St & Ore**	17	24-Feb-21	17-Mar-21			17-Feb-21	10-Mar-21	
MP3D2-100	Install Maintenance of Traffic, Erosion/Sediment Control Devices; Test Pit	2	24-Feb-21	27-Feb-21			17-Feb-21	19-Feb-21	0%
MP3D2-101	Remove Existing Trees	2	24-Feb-21	27-Feb-21			17-Feb-21	19-Feb-21	0%
MP3D2-102	Install Watermain, Fire Hydrants, Gate Valves, Fittings & Appurtenances	15	27-Feb-21	17-Mar-21			19-Feb-21	10-Mar-21	0%
MP3D2-105	Install Electric Manholes, Conduits, and Concrete Enclosures (Tennyson St to Unicorn Ln)	5	27-Feb-21	05-Mar-21			25-Feb-21	04-Mar-21	0%
MP3D2-106	Install Electric Manholes, Conduits, and Concrete Enclosures (Unicorn Lane to Oregon Kn	5	05-Mar-21	11-Mar-21			04-Mar-21	10-Mar-21	0%
MP3D2-107	Install Catch Basins, Basin-Connect & Sewer Pipes, and Manholes	5	05-Mar-21	11-Mar-21			04-Mar-21	10-Mar-21	0%
DCKA2019C0002-LA14.3.3.1	**Phase 3A (Bridge Reconstruction of Pinehurst Branch)**	0							

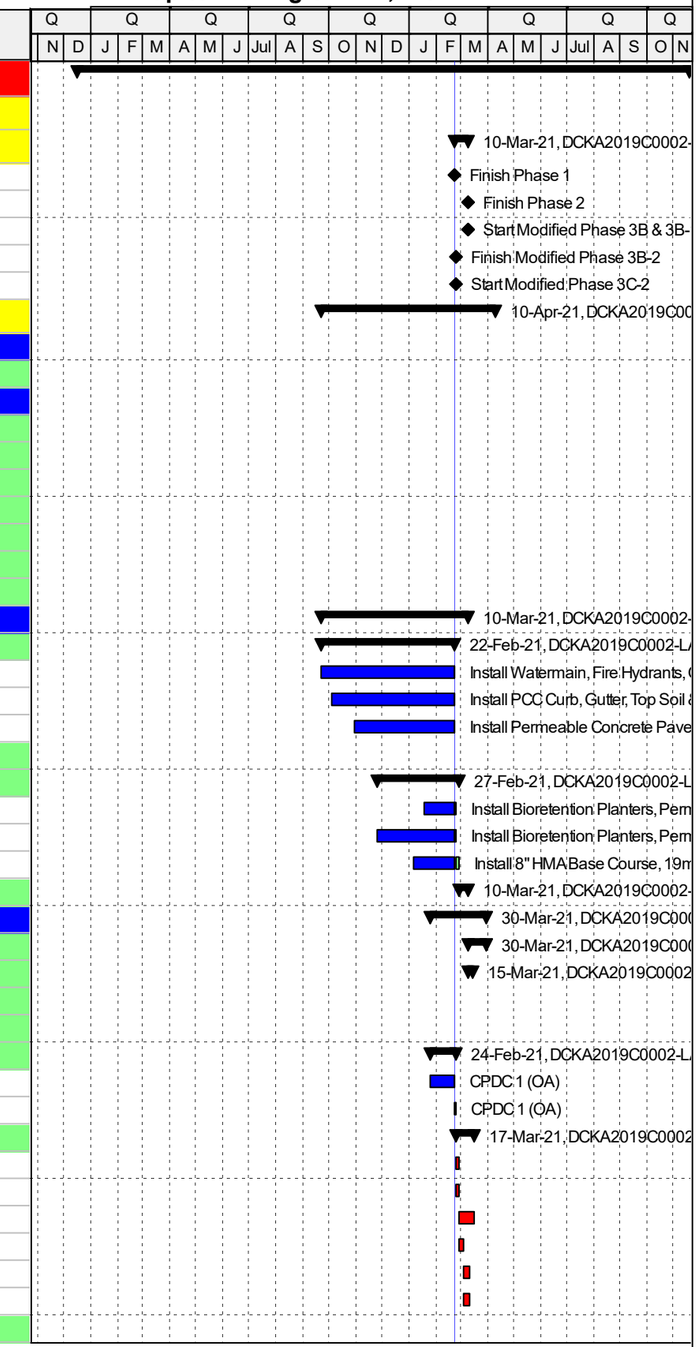

Remaining Level ...
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD02-24-21)

DCKA2019C0002-LA14

3-Week Look-Ahead© Oracle Corporation

CAPITOL PAVING OF D.C., INC. WASHINGTON, D.C. 20018 202 - 529-7225

Data Date: 22-Feb-21

Capitol Paving of D.C., Inc.

Activity ID	Activity Name	Original Duration	Early Start	Early Finish	Actual Start	Actual Finish	Late Start	Late Finish	Activity % Complete
DCKA2019C0002-LA14.3.3.1.1	Bridge Work	0							
DCKA2019C0002-LA14.3.3.1.2	Utility Work & Civil Work	0							
DCKA2019C0002-LA14.3.3.8	Phase 3E (Entire Roadway Section b/w Oregon Knolls Dr & Private Drivew	0							
DCKA2019C0002-LA14.3.4	Traffic & Streetlight Work	25	22-Feb-21	10-Apr-21	04-Nov-20		15-Sep-21	05-Nov-21	
TR-1000	Remove Existing Streetlights & Install New Poles,Arm, Luminaires (Phase 1) Western Ave	7	22-Feb-21	02-Mar-21			15-Sep-21	23-Sep-21	0%
TR-1010	Remove Existing Streetlights & Install New Poles,Arm, Luminaires (Phase 1) Dogwood St	7	03-Mar-21	10-Mar-21			23-Sep-21	04-Oct-21	0%
TR-1020	Remove Existing Streetlights & Install New Poles,Arm, Luminaires (Phase 2) Rittenhouse S	7	11-Mar-21	18-Mar-21			04-Oct-21	13-Oct-21	0%
TR-1050	Install Traffic Foundation, Cabinet, Controller, Pole, Lights (Oregon Ave & Military Rd)	14	27-Mar-21	10-Apr-21	04-Nov-20		21-Oct-21	05-Nov-21	20%
DCKA2019C0002-LA14.3.5	Paving, Line Stiping, Signage, and Miscellaneous Work	25	27-Feb-21	11-Mar-21	28-Dec-20		15-Oct-21	30-Oct-21	
DCKA2019C0002-LA14.3.6	Landscape Work	5	24-Feb-21	03-Mar-21			16-Nov-21	22-Nov-21	
DCKA2019C0002-LA14.4	LUMPSUM ITEMS (Non-Construction)	1	22-Feb-21	19-Nov-21	16-Dec-19		16-Dec-19	04-Dec-21	
DCKA2019C0002-LA14.5	POST-CONSTRUCTION PHASE	0							
DCKA2019C0002-LA14.6	Delays, Additional Work, and Changes	5	22-Feb-21	27-Feb-21			30-Oct-21	05-Nov-21	

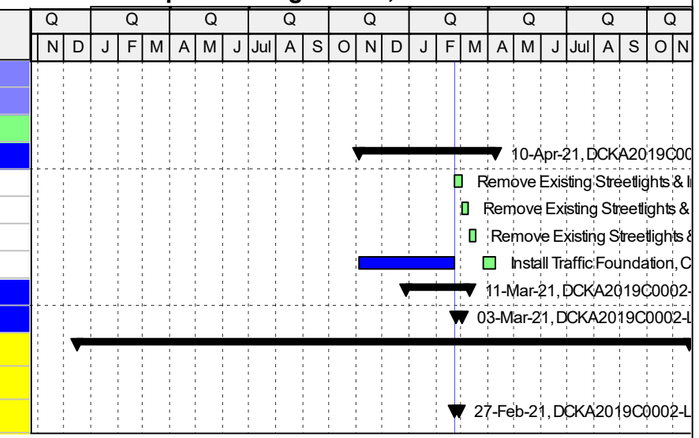

Remaining Level ...
Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining ...

Reconstruction of Oregon Ave NW Look-Ahead Schedule (DD02-24-21)

DCKA2019C0002-LA14

3-Week Look-Ahead© Oracle Corporation
